Development of Container Terminal at Kamarajar Port on DBFOT basis
CONSTRUCTION PROGRAM

Concessioning Authority M/s Kamarajar Port Limited (KPL)
Concessionaire M/s Adani Ennore Container Terminal Pvt. Ltd. (AECTPL)
Independent Engineer M/s Engineers India Limited (EIL)
Concession Agreeement Dated 15.03.2014
Concession Value Rs. 724 Cr.
Period of Completion 27 Months

Progress as on 31st Oct-2016=96.33%

ID	Task Name	Durati on (days)	Start Date	Finish Date
	Phase-1 (400m x 500m)			
1	Construction of Main Berth	728	17-11-14	14-11-16
		441	20-10-14	04-01-16
2	Casting of Precast elements and placing	442	28-05-15	12-08-16
		408	27-10-15	09-12-15
3	Deck Fittings	414	1-07-15	18-08-16
		138	5-06-15	21-10-15
4	Back up yard development	781	15-11-14	4-01-17
		444	20-10-14	7-01-16
5	Utility Buildings	529	15-12-14	27-05-16
		363	22-11-14	20-11-15
6	Installation of Electrical & IT Works	466	16-03-15	24-06-16
		326	23-02-15	15-01-16
7	Equipments	95	15-09-16	19-12-16
		100	17-10-15	25-01-16
8	Commissioning of Terminal	48	3-12-16	20-01-17
		6	25-01-16	30-01-16

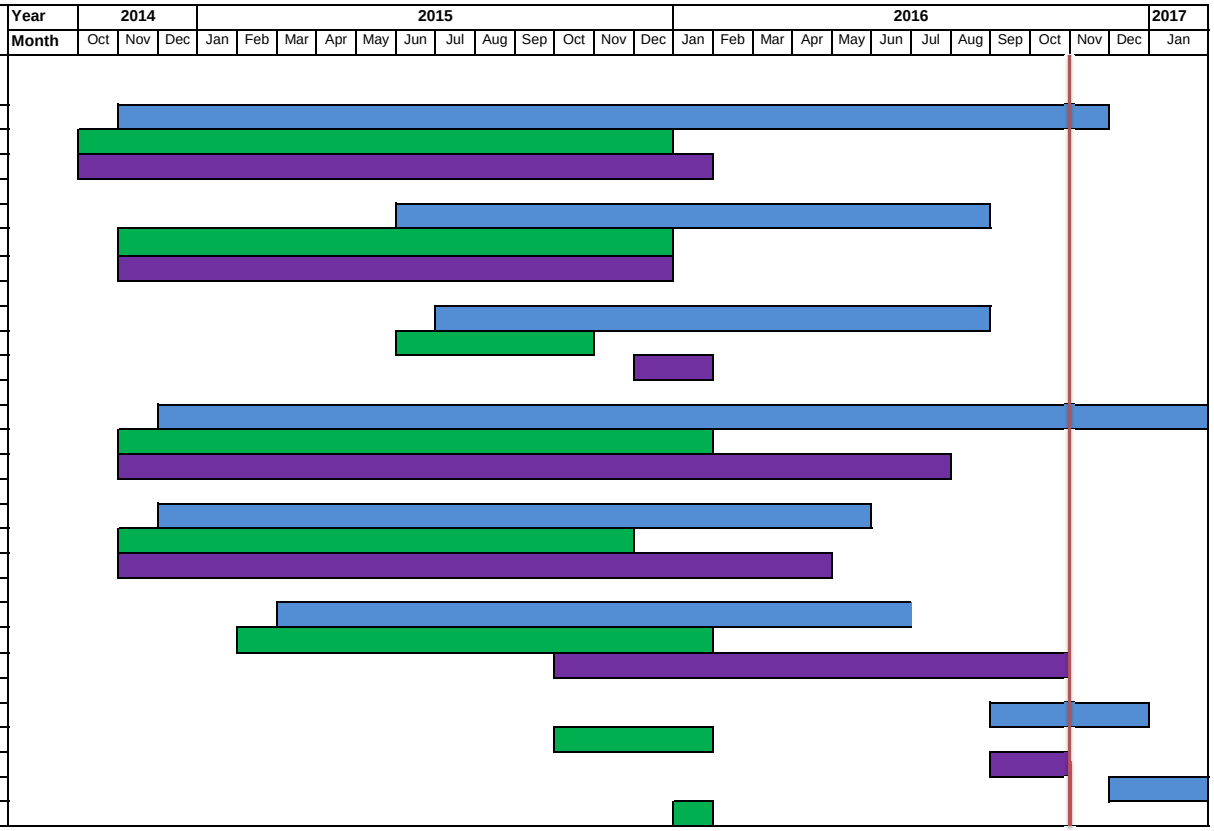

PLANNED
TARGET
ACTUAL
